



Meadow Creek Valley Implementation Phases

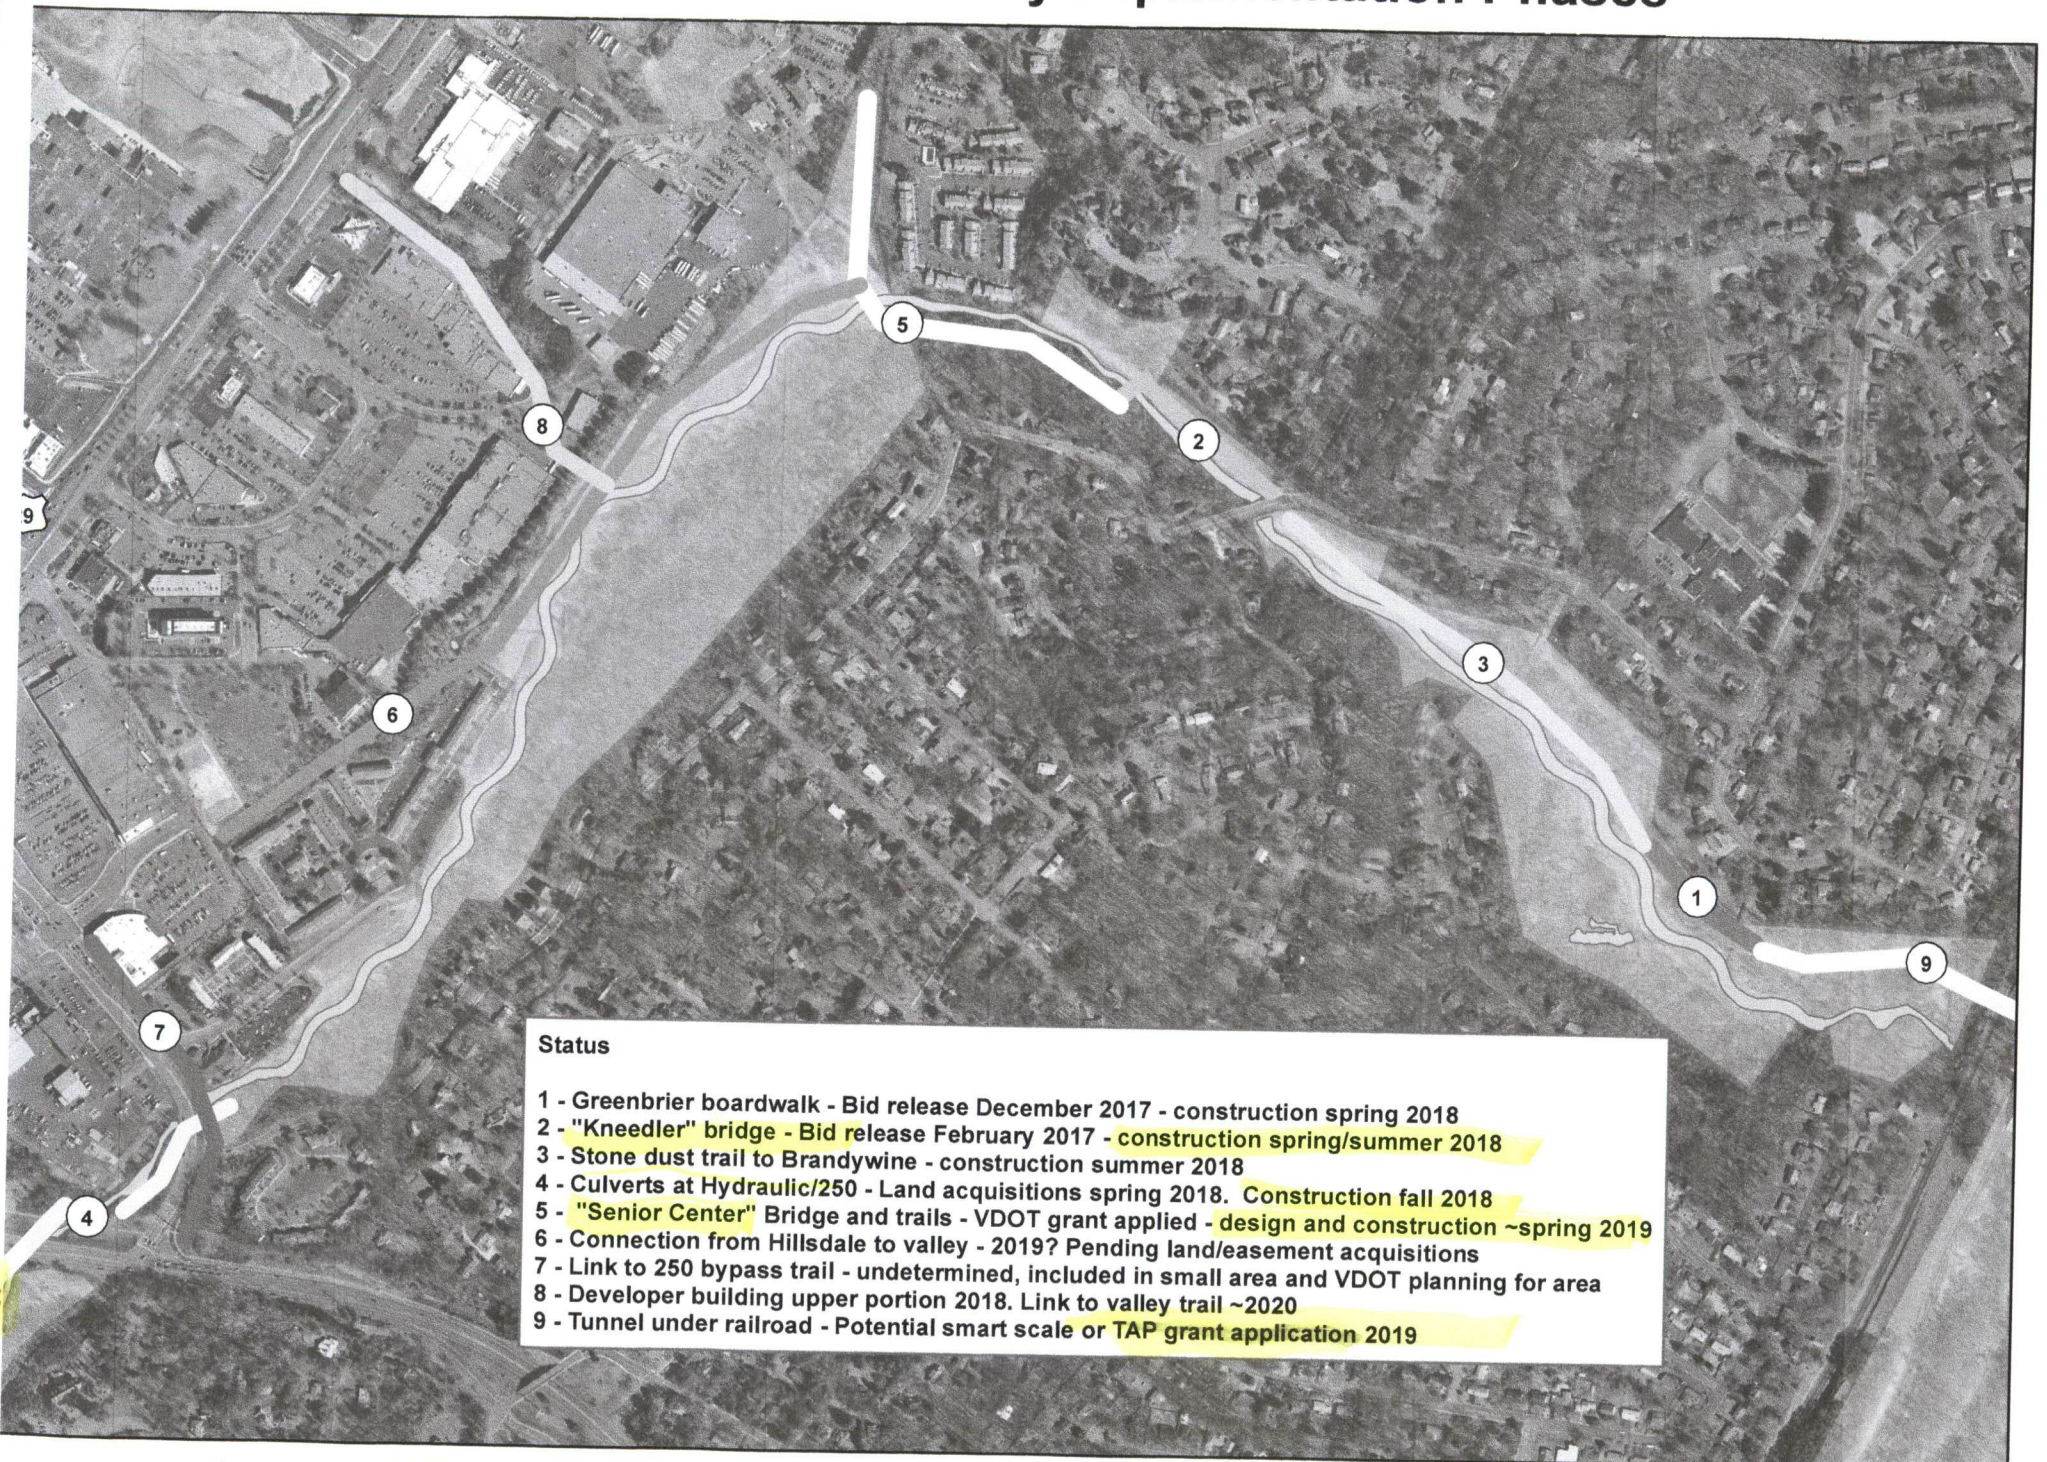

- Status**
- 1 - Greenbrier boardwalk - Bid release December 2017 - construction spring 2018
 - 2 - "Kneeder" bridge - Bid release February 2017 - construction spring/summer 2018
 - 3 - Stone dust trail to Brandywine - construction summer 2018
 - 4 - Culverts at Hydraulic/250 - Land acquisitions spring 2018. Construction fall 2018
 - 5 - "Senior Center" Bridge and trails - VDOT grant applied - design and construction ~spring 2019
 - 6 - Connection from Hillsdale to valley - 2019? Pending land/easement acquisitions
 - 7 - Link to 250 bypass trail - undetermined, included in small area and VDOT planning for area
 - 8 - Developer building upper portion 2018. Link to valley trail ~2020
 - 9 - Tunnel under railroad - Potential smart scale or TAP grant application 2019



Bicycle and Pedestrian Master Plan Status Update (as of July 2018)

In September 2015, the City Council adopted the Bicycle and Pedestrian Master Plan as an amendment to the City's Comprehensive Plan (2013). The Bicycle and Pedestrian Master Plan will guide decisions related to bicycle and pedestrian infrastructure and design, safety, access, and more. It includes a list of potential bicycle and pedestrian projects that the City will consider over time. This document provides a status update on the proposed projects included in the plan for the purposes of discussing CIP priorities in FY2019.

The following tables are taken directly from the Bicycle and Pedestrian Master Plan as adopted in 2015. Note that some sidewalk locations/facility types may have changed since the adoption of the plan as a result of additional field work/public process/design.

Meadow Creek (Pen Park)	Multi Use Path	Developer to build bridge in 2018, City working to build section from Pen Park to Rio Road in 2018
Meadow Creek	Culvert Trail	Design phase and working to finalize acquisition of land in 250/hydraulic triangle City to submit Smart Scale application in 2018. Greenbrier Park trail under construction now, "Knedler" bridge to be bid late summer 2018. Senior center Bridge design to begin Fall 2018
Riverview to Pantops	Bridge over Rivanna River	No progress. Will require major grant for design/construction. PDC Smart Scale Grant submitted for Free Bridge. Not awarded

City of Charlottesville

Parks and Recreation Advisory Board – Agenda Item

July 11, 2019

PRESENTATION – 1

Aquatic Operations & Training

Staff from Aquatics will provide an overview of 2019 season facility operations and training programs.

PRESENTATION – 2

Citywide Trail & Connectivity Issues

Staff will provide an overview of current citywide trail and connectivity initiatives.

INFORMATION - 1

Meadow Creek Valley Master Plan Implementation

Below is an outline of the current status of efforts in the Meadow Creek Valley

- Greenbrier Park Trail improvements
 - Construction complete –some touch up items and E&S silt fence removal remain
 - Working with City to determine solution to historic stormwater issues at 3 way stop
- Kneedler bridge moving forward
 - Final ramp design and local flood permit approval underway now
 - (FEMA final stamp due August)
 - Will need bid review by DCR (state grant funding agency)
 - Construction anticipated to begin fall 2019
- Funding to build senior center bridge awarded in VDOT TAP application
 - Design RFQ summer 2019 - Construction anticipated by Spring 2020
 - Easement from Republic Homes acquired March 2019 (Greenbrier Drive end of trail)
- Coordinating with developer and The Nature Conservancy on options for connection from Michie & Hillsdale to north end at Senior Center bridge.
- TAP grant application submitted to connect 250 bypass trail to Hydraulic av Michie Drive (2019)
- Continue to work to finalize land donations in 250/Hydraulic/29 triangle
- Norfolk Southern Railroad tunnel
 - (VDOT) grant application not funded for next TAP round (2019).
 - Will continue to work to identify funding
